

PPODs Managing Small Secondary Payloads

Garrett L. Skrobot

Mission Manager
Flight Projects Office
Launch Services Program

February 26-27, 2008



Introduction


- What is LSP's History with Small and Auxiliary Payloads?
- What has been some of the challenges with managing Auxiliary payloads?
- What work has LSP provided in looking at getting Auxiliaries on Launch Vehicles?
- What is a PPOD?
- How will these Auxiliary Payloads be managed?
- Concepts on how the selection of an Auxiliaries could be managed to fly on LV's



Recent History of NASA's Small Satellite Missions

John F. Kennedy Space Center

Secondary	Approx.	Primary					
Payload	Mass	Date	Vehicle	(Customer/Payload)	Type		
DUVE	102 kg	07/92	Delta II/6925	NASA/GEOTail	2 Non Separating		
SEDS-1	45 kg	03/93	Delta II/7925	USAF/NAVSTAR II-19	Tether		
PMG	55 kg	06/93	Delta II/7925	USAF/NAVSTAR II-21	Tether + Diagnostics		
SEDS-2	50 kg	03/94	Delta II/7925	USAF/NAVSTAR II-21	Tether		
SURFSAT	35 kg	11/95	Delta II/7920	CSA/RADARSAT	2 Non Separating		
SEDSAT	40 kg	10/98	Delta II/7326	NASA/DeepSpace-1	Separating		
Orsted	61 kg	02/99	Delta II/7920	USAF/P-91	Separating		
Sunsat	63 kg	02/99	Delta II/7920	USAF/P-91	Separating		
ACRIM	120 kg	10/99	Taurus (T-4)	Commercial/KOMPSAT	APC/Separating		
Munin	6 kg	11/00	Delta II/7320	NASA/EO-1&SAC-C	Separating		
Starshine 3	100 kg	09/01	Athena I	USAF/PICOSAT/PCSat/SAPPHIRE	Separating		
QuikTOMS	375 kg	10/01	Taurus (T-6)	Commercial/OrbView-4	APC/Separating		
CHIPS	~85kg	01/03	Delta II/7320	NASA/ICESat	Mini-DPAF/Sep		
ST-5	~120kg	03/06	Pegasus	NASA	Separating		
	_						

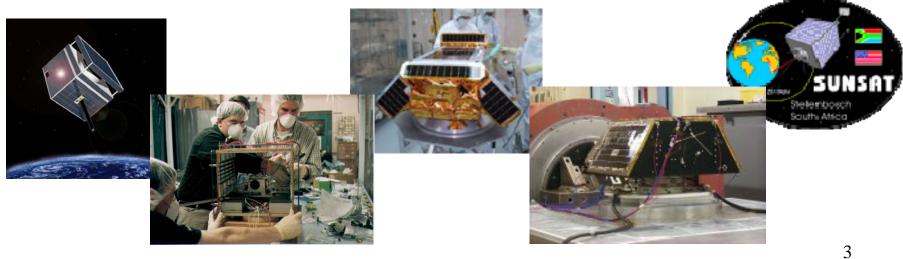



Auxiliary Payload Challenges

- Auxiliaries being ready and on time to fly on the day of launch
- Understanding of what is required from the secondary for inputs into testing and reports
- Knowing that they are the auxiliary and not a primary
- Funding, there are costs associated with integrating an auxiliary to the launch vehicle
- Interface requirement, the auxiliary initially indicates that all that is required is a separation circuit and later asking for a quick disconnect purge system in a Class 10K clean room
- Convincing the Primary that the auxiliary payload has been well analyzed and the mission risk mitigated



Past Studies and Agreements

- February 1992 Memorandum of Agreement between Space System Division Delta II Systems Program Office and NASA Orbital Launch Services Project for Secondary Mission on Delta II was signed
- August 1992 First Copy of the Secondary Payload Planner's Guide on Delta II was provided
- February 2002 Feasibility Study was performed to integrate PPODs and BioNanoSat as a secondary on Pegasus
- April 2003 Secondary Payload Capability Study conducted for both Atlas V and Delta IV
- 2005 LSP provides funding for Wallops to develop the Multi Payload Adapter to support possible DARPA launch opportunities
- January 2006 Request for Launch Services Proposal (RLSP) for the Lunar Reconnaissance Orbiter (LRO) mission included requirements for accommodating at least one secondary payload mission, with options to accommodate multiple payloads up to a total capability of 1000 kgs



Present Work

Launch Services Program

Atlas V

- March 2007 Submitted Statement of Work (SOW) to ULA Atlas to develop a method to integrate PPOD on the Atlas V
 - This study kicked off on April 23 with the first out brief at the end of June
 - Current plan is to complete the Atlas V development and integration, then start the Delta IV effort
 - » SOW to proceed to Preliminary Design Review (PDR) is in proposal phase





Present Work

Launch Services Program

Taurus XL

- April 2007 Started working with Orbital Sciences Corporation in developing a method to integrate PPODs on the Taurus XL
 - OSC completed feasibility study and SOW is complete
- January 2008 Started the development work to implement PPODs on the OCO and Glory mission – Awaiting final approval from Science Mission Directorate and Flight Planning Board to fly PPOD on these two missions
- If we implement the PPOD system on these ELVs, are there opportunities to fly this system?





Opportunities

FPB Approved 11/01/07	2007	2008	2009	2010	2011	2012	2013	2014	
Release 12/03/07							21 Q2 Q3 Q4 Q1 Q2 Q3 Q4 Q1 Q2 Q3		
Small Class (SC)		A IBEX (I							
Pegasus (P)	AM (P) 4/25/07	OCO (T) V 12/15/08 V	√	Possil	he AF N	lissions	not lis	ted?	
Taurus (T)	,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,	GLORY (1) 12/15/08	5	1 0001			not no		
			MOAA-N' (D3) 2/1/09						
Medium Class (MC)	A THEMIS (D) 2/17/07	A STSS (D) 4/1/08	A KEPLER (D) 2/16/09					ı	
Delta 732X Series (D3)	OENIX (D) A 8/4/07	A W STSS ATF	RR A NPP (D) UR) A 4/30/09					ı	
Delta 742X Series (D4)	DAWN (DH) A 9/27/07	A GLAST (5/29/08	(DH)	A AQUARI A 5/23/10	US (D3)			I	
Delta 792X Series (D)		A OSTM (1 6/15/0	D3) 8					ı	
Delta 792X H (DH)		TBD (DH)	WISE (D3)					I	
Intermediate (IC) / Heavy Class (HC)	3	△ GOES-O (DI 4/2008	V) GOES-P (DIV 4/2009	")					
Atlas V (AV)	LRO/LO	 CROSS (AV)	MADS SCIENCE		LDCM (AV) 1/2011 Juno (AV) \(\triangle \)			ı	
Delta IV (DIV)	1	SDO (AV) \triangle^{A}	MARS SCIENCE LAB (AV) NET 9/15/09	•	8/11/2011 <u></u>		JWST (Ariane) 6/2013	ı	
Delta IV Heavy (IVH)								ı	
COTS NOTE: COTS Demo launch dates shown		SpaceX-1	SpaceX-2 2-Qtr/200						
for informational purposes only - LSP does not control these dates.		3-Qtr/2008		eX-3 ·/2009				ı	
Vehicle Unassigned					(△ RBSP 3/2012	△ SMEX-13 4/2013	△ SMEX	
If we implement	the PPC	DD svste	em on E	LV's.		SMEX-12 △ 4/2012	TDRS-L	△ GPI 6/2	
			is syste		Öiscovery 11△ □ 9/2011 △	Discovery - 12		MMS 10/2014	



So, What is the PPOD?



PPOD Concept

- The Concept for PPOD on LV's is to perform a source development and not a point solution
 - This would allow late change out of payloads without having to re-run analysis
 - Once the LV knows that a PPOD will fly on their mission, the information for that PPOD is already known even if the payloads in side are not
- The PPOD to LV ICD will call out the tolerances for mass and CG for the payload
 - When the payloads are being designed, they will need to be designed to the PPOD standard
- Standardization is key to reducing integration time and cost



PPOD Overview


- The Poly Pico satellite Orbital Deployer (PPOD) was developed by California Polytechnic State University (Cal Poly) in support to the Stanford University CubeSat program
- PPOD is a standard deployment system
 - Standard deployer ensures all CubeSat developers conform to common physical requirements, to minimize cost and development time
- The PPOD is the interface between the launch vehicle and CubeSats
 - The PPOD is versatile, with its small profile and ability to mount in a variety of configurations






PPOD Overview

- The PPOD utilizes a tubular design and can hold up to 34cm x 10cm x 10cm of hardware
 - The most common configuration is three Pico satellites of equal size; however, the capability exists to integrate Pico satellites of different lengths
 - PPOD (empty) is ~2.5 kg
 - Typical CubeSats are ~1 kg each
 - » Up to 3 kg for a triple like GeneSat
 - » Working to have total mass at <10kg</p>
- The tubular design creates a predictable linear trajectory for the CubeSats resulting in a low spin rate upon deployment
 - The satellites are deployed from the PPOD by means of a spring and glide along smooth flat rails as they exit the PPOD
 - After a signal is sent from the Launch Vehicle (LV), a spring-loaded door is opened and the CubeSats are deployed by the main spring

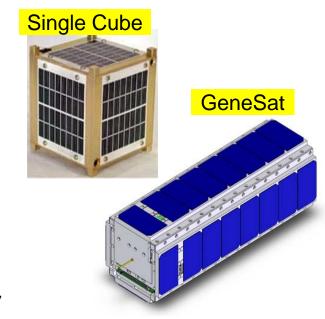





Flight History and NASA Involvement

John F. Kennedy Space Center

- The PPOD system has flown on 3 different types of Launch Vehicles to date:
 - **Eurockot**, 2003
 - Dnepr, 2006, 2007
 - Minotaur, 2006 NASA GeneSat mission (Ames)
- Upcoming launches scheduled for NASA PPOD missions:
 - Minotaur, 2008
 - Falcon, 2008





How will it be Managed as an Auxiliary Payload?




System Design Requirements

- Top-Level requirements were established:
 - PPOD shall not impact the primary payload (physically or functionally)
 - PPOD shall not impact heritage avionics qualification status or architecture (focus of concern is the affect of a localized added mass)
 - PPOD shall not impact the performance or reliability of the existing hardware and vehicle design
 - Design solution shall minimize interfaces with flight critical hardware
 - Implementation shall be non-mission specific
 - Integration and test design shall not interfere or disrupt normal Launch Vehicle or primary payload operations
 - Integration shall allow for full PPOD testability
 - Standard integration and test flow shall not be impacted by PPOD integration



Management Structure


- With Auxiliary PPOD systems being a low cost solution to fly experiments, management and the technical team needs to be different then the current classical way of integration
- Synergy from the primary payloads needs to incorporate to ensure that Auxiliary Payload requirements are met

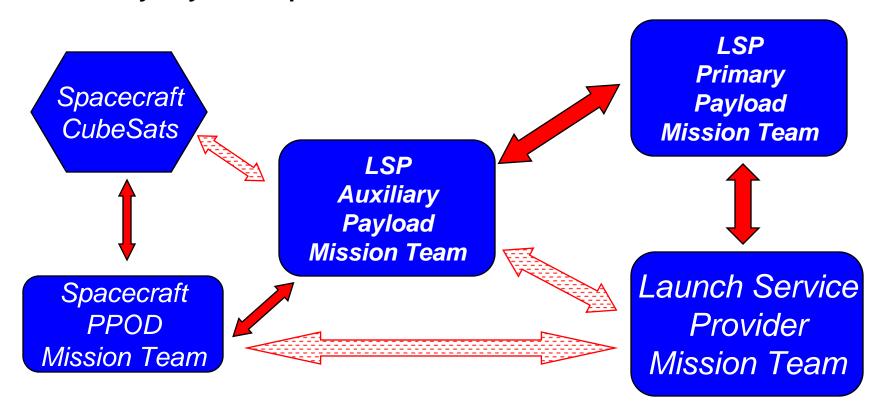



Auxiliary Payload Risk

- The Primary Payload will see the Auxiliary as an element of risk to their mission
- These risks have to be managed so they can be reduced or even mitigated completely for the Primary to accept the Auxiliary onto the mission

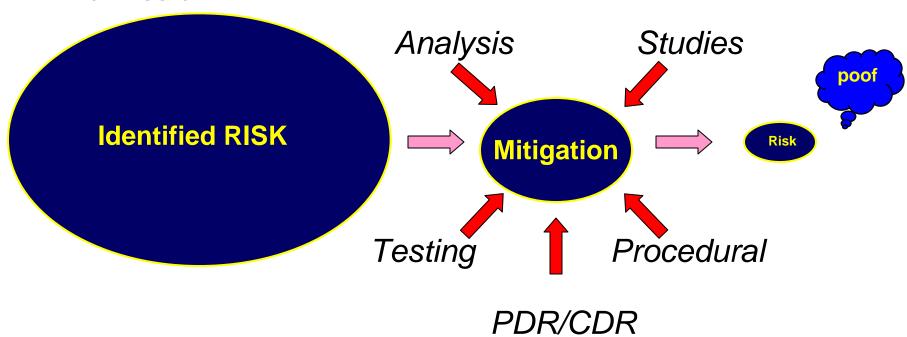




Auxiliary Payload Risk

Launch Services Program Risk
 Management Plan LSP-PLN-353.01 is the document that is used to manage risk

Launch Services Risk Exposure Matrix

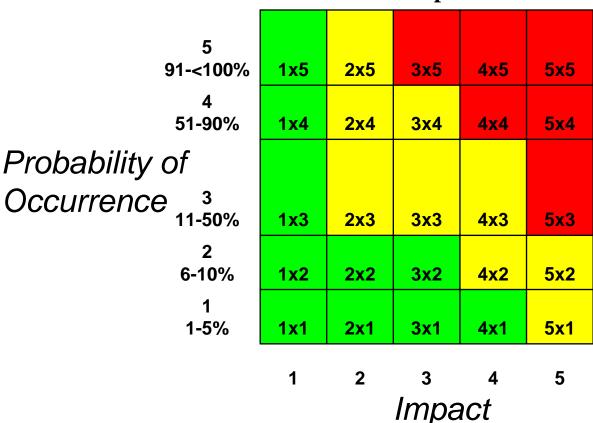

- Identify the Risk
 - Statements of risk
 - List of Risks
- Each Risk will be analyzed to determine classification and prioritization
- Plan Decide what should be done about risk
 - Mitigation strategy and plans
 - Acceptance rationale and tracking requirements
 - Track Monitor risk metrics and verify/validate mitigation actions
 - Report status on risk and migration plan
 - Control Decide to re-evaluate and replan mitigations, close risks, invoke contingency plans, or continue to track risks
 - Risk Decisions



Managing Schedule

Launch Services Program Top-level schedule targets Risk for Development of Taurus Mitigation system SC Start **PDR** Selection CDR Development L-10 L-8 L-6 Decision by Prim SC To Fly Auxiliaries L-9.5 **PPOD** SC Readiness Integrate SC Delivered to Review Into PPOD Site ILC L-3 L-2 L-1 L-0



The NASA Project Life Cycle

NPR 7120.5D, Figure 2-4

		Lauticii Services Program						
NASA Life Cycle Phases	Pre-Systems	FORMUI Acquisition	-ATION Appr Impler	oval for nentation System	IMPLE as Acquisition	MENTATION Operations	Decommissioning	
Project Life Cycle Phases	Pre-Phase A: Concept Studies	Phase A: Concept & Technology Development	Phase B: Preliminary Design & Technology Completion	Phase C: Final Design & Fabrication	Phase D: System Assembly, Int & Test, Launch	Phase E: Operations & Sustainment	Phase F: Closeout	
Project Life Cycle Gates & Major Events	KDP A FAD Draft Project Requirements	KDP B Preliminary Project Plan	KDP C Saseline Project Plan	KDP D	KDP E	KDP F End of Mission	Final Archival of Data	
Human Space Flight Project Reviews ¹ Re-flights	ASPMO	R ASM SRR SDR (PNAR	PDR (NAR Re-enters appropriate life modifications are needed	cycle phase if	SAR ORR FRI Inspections and Refurbishment	PLAR CERR ³ End of Flight	DR	
Mission Project Reviews ¹ Launch Readiness Reviews	<u>∠</u> MC	ASM SRR MDR ⁴ (PNAR)	PDR (NAR	CDR / SI	R ORR FF	R PLAR CERR ³ SMSR, LRR (LV), FRR (LV)	DR	
Supporting Reviews		Peer	Reviews, Sub-sys	tem PDRs, Sub-sy	stem CDRs, and Sys	tem Reviews		
FOOTNOTES 1. Flexibility is allowed to the timing, number and content of reviews as long as the equivalent information is provided at each KDP and the approach is fully documented in the Project Plan 2. PRR needed for multiple system copies. Timing is notional. 3. CERRs are established at the discretion of Program Offices. 4. For robotic missions the SRR and the MDR may be combined. ASP—A ASM—A CDR—C CERR—DR—De FAD—F FAD—F FAD—F FAD—F FAD—F FAD—F FAD—F FRR—L MCR—M MDR—M					ACRONYMS ASP—Acquisition Strategy Planning Meeting ASM—Acquisition Strategy Meeting CDR—Critical Design Review CERR—Critical Events Readiness Review DR—Decommissioning Review FAD—Formulation Authorization Document FRR—Flight Readiness Review PLAR—Post-Launch Assessment Review PNAR—Preliminary Non-Advocate Review PNAR—Production Readiness Review SAR – System Acceptance Review SDR—System Definition Review SDR—System Integration Review SMSR—Safety and Mission Success Review SRR—System Requirements Review			



Why Develop Auxiliary Carriers?

John F. Kennedy Space Center

Launch Services Program

NASA's Strategic Goals

Strategic Goal 1: Fly the Shuttle as safely as possible until its retirement, no t later than 2010.

Strategic Goal 2: Complete the International Space Station in a manner consistent with NASA 's International Partner commitments and the needs of human exploration.

Strategic Goal 3: Develop a balanced overall program of science, exploration, and aeronautics consistent with the redirection of the human spaceflight program to focus on exploration.

Strategic Goal 4: Bring a new Crew Exploration Vehicle into service as soon as possible after Shuttle retirement.

Strategic Goal 5: Encourage the pursuit of appropriate partnerships with the emerging commercial space sector.

Strategic Goal 6: Establish a lunar return program having maximum possible

utility for later missions to Mars and other destinations.

"Everyone in the Launch Services Program strives to meet our customers' needs by providing mission assurance through reliable expertise."

~ Steve François

"To pioneer the future in space exploration, scientific discovery, and aeronautics research."

➤ NASA's Mission

LSP's Vision: To be the recognized leader in launch services

LSP's Mission: Leadership and expertise in providing on -orbit, on-time, on-cost launch services

LSP's Goals

Goal 1: Maximize successful delivery of spacecraft to space

Goal 2: Assure launch services for all customers – now and in the future

Goal 3: Promote evolution of a competitive space market

Goal 4: Continually enhance LSP's core capabilities

2007 Path to the Future



Manifesting Process for CubeSats on NASA missions


IN DEVELOPMENT



- With the increase in the CubeSat spacecraft in the space community, LSP is developing the capabilities to fly these payloads on ELV missions with excess margin
 - Who will fly and who will determine which one will be manifested?
- Since these missions are not the traditional NASA payload (SMEX, Explorers, etc), the current process which NASA manifests missions is not the best method to manifest



- The Space Development and Space Wing uses a process called SERB (Space Experiments Review Board) to prioritize missions
- The SERB reviews all the DoDsponsored science experiments submitted via the service boards (i.e., Army, Navy, and Air Force) and other related organizations, e.g., the MDA, and prioritize them according to various criteria. The experiment ranking is based on military relevance 60%, service priority 20%, and technical merit of experiment 20%.

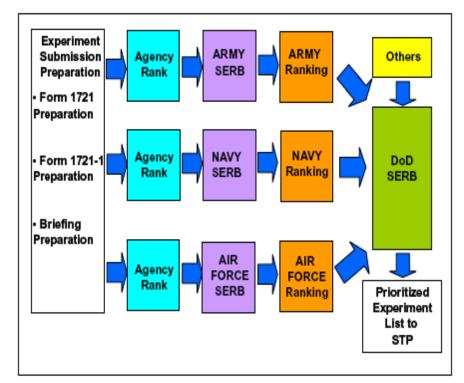



- The Space Development and Space Wing SERB process has been a successful method to determine the priorities for their small payloads
- With this success, NASA should adopt a method similar to the SD&TW model in the selection and manifest of our small payloads
 - By adopting this model, NASA and DoD will be working to the same process
 - Having the same process will allow NASA and DOD a better partnership with respect to small auxiliary payloads
 - One difference between the DoD SERB and a NASA process is that DoD provides funding for the experiment. This will not be the case for the NASA spacecraft
 - » The auxiliary payload will be responsible for their own funding




- Selection of a Mission
 - Once a year, each Directorate (SMD, SOMD, ESMD, and SD&TW) will bring forward their sponsor auxiliary payload that they would like to be ranked
 - Once a mission has been identified to have available margin to fly an auxiliary payload, one is selected from the ranking list
- Evaluation Process will be used to determine which mission will be selected to accommodate one of the slots
 - Each candidate SC shall be graded on a set of evaluation criteria
 - » 50% Does the SC meet the Visions and Goals of the Agency
 - » 25% The technical advancement
 - » 25% Educational



Method to Evaluated Auxiliary Payloads on ELV's

Launch Services Program

 Each organization shall provide a POC to the board that will work with the their auxiliary payload to coordinate the preparation and submission

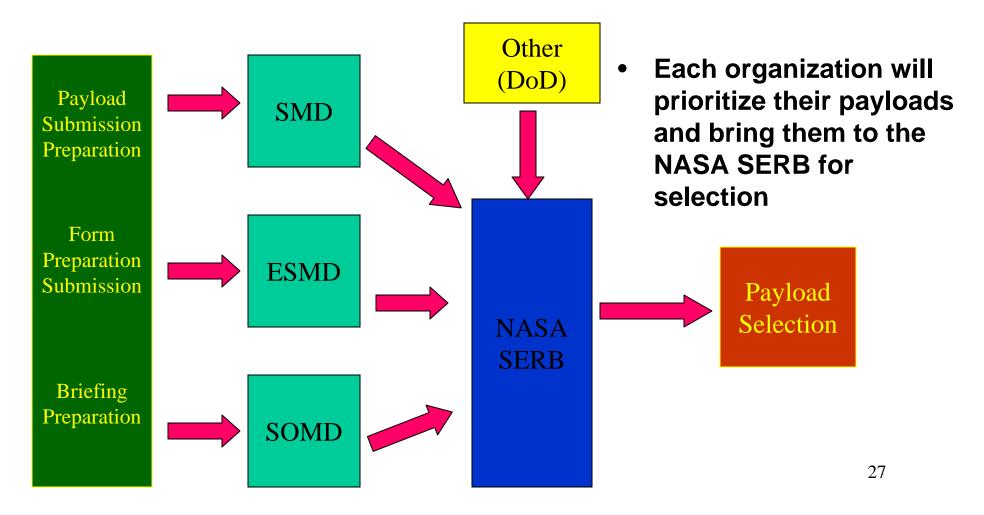



Development of the NASA SERB


Launch Services Program

The NASA SERB will consist of five organizations

 Each organization shall provide two representatives to participate in the evaluation

 Launch Services Program acts as the SERB Committee Chair for the Evaluation process

 Each payload will be evaluated by the selection criteria

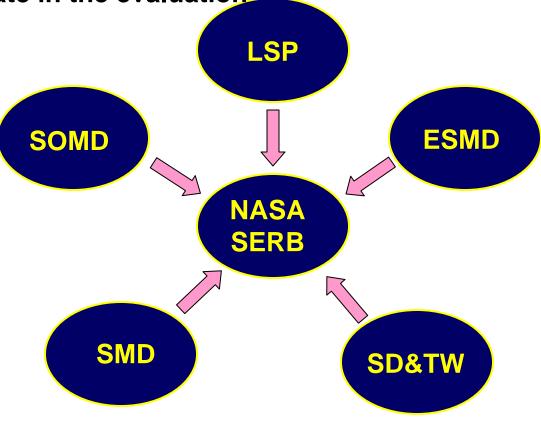



Work Still Needing to be Performed

- Continue the Management of the PPOD development of ELV's
- Continue the coordination with the Primary to show the mitigation of Mission Risk
- Bring overall concept and manifesting processes to a special Flight Planning Board (following a preliminary design review)
- Develop the NASA SERB Process and Schedule
 - Pre- Manifest
 - Manifest
 - Post Manifest



Work Still Needing to be Performed

- Develop the Auxiliary Payload Manifesting Policy
- Selection Criteria
 - » 50% Does the SC meet the Visions and Goals of the Agency
 - » 25% The technical advancement
 - » 25% Educational
- Brief each of the Stakeholders and incorporate comments
- Submit for Process to the Fight Planning Board for approval
- How will the Integration team support the mission
 - Use the same team as the primary?
- LSP continues to investigate new and innovative ways to increase our capability to place NASA payloads in orbit
